


Activity ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	2019																							
						AUG				SEP				OCT				NOV				DEC							
						12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23				
1000	PH 2- 3 MANHATTAN -WATROUS -DALE MABRY	0	221	23/AUG/19	26/NOV/20	[Summary bar]																							
1005	Tree Trim / Removal	6	0	03/SEP/19	10/SEP/19	[Progress bar]																							
1006	Utility Exploration Existing Lines	10	0	13/AUG/19	26/AUG/19	[Progress bar]																							
1008	Set MOT at Manhattan / Estrella intersection	1	0	05/AUG/19	05/AUG/19	[Summary bar]																							
1010	Water Main Manhattan / Estrella Intersection	4	0	19/AUG/19	21/OCT/19	[Progress bar]																							
1012	Water Main Manhattan / Neptune intersection	22	0	04/NOV/19	06/DEC/19	[Progress bar]																							
1015	800' Water Main from Estrella St. to NeptuneSt.	12	0	08/AUG/19	23/AUG/19	[Progress bar]																							
1025	320' WM to Zelar St. and crossing	12	0	21/OCT/19	26/NOV/19	[Progress bar]																							
1028	Water Main at Watrous Intersection	10	0	15/OCT/19	18/NOV/19	[Progress bar]																							
1030	Sewer Pipe - 3 MH stub up @ Watrous Intersection	8	0	06/JAN/20	15/JAN/20	[Progress bar]																							
1033	Install 300"- 6" W M & Fht Jetton to Watrous.	18	0	11/NOV/19	04/DEC/19	[Progress bar]																							
1035	Set MOT Sta 201+80 to Neptune ST. Box Culvert	1	0	05/SEP/19	05/SEP/19	[Summary bar]																							
1038	Install 560' Box Culvert to Neptune St.	23	0	17/SEP/19	23/OCT/19	[Progress bar]																							
1043	Flowable Fill at exist. Sewer 206+80 to 208+80	5	0	23/SEP/19	27/SEP/19	[Progress bar]																							
1045	Storm System & J Box & 43x68 ERCP @ Neptune	12	0	07/OCT/19	22/OCT/19	[Progress bar]																							
1048	Install Pervious Pavement	10	0	07/OCT/19	10/OCT/19	[Progress bar]																							
1049	Install Curvb/Sidewalk /Driveway to Neptune	8	0	06/JAN/20	15/JAN/20	[Progress bar]																							
1050	Road base Material	15	0	24/OCT/19	29/OCT/19	[Progress bar]																							
1055	First Lift of Asphalt to Neptune intersection .	2	0	02/JAN/20	03/JAN/20	[Progress bar]																							
1058	Set MOT Neptune to Watrous	1	0	11/NOV/19	11/NOV/19	[Summary bar]																							
1060	Install 600' Box Culvert Sta. 209 to Watrous	46	0	21/OCT/19	19/DEC/19	[Progress bar]																							
1062	Install Storm Drainage System	34	0	18/FEB/20	20/FEB/20	[Progress bar]																							
1064	Install box culvert @ Watrous Intersection	12	0	17/FEB/20	20/FEB/20	[Progress bar]																							
1075	Utility Connections at Watrous intersection	12	0	11/FEB/20	26/FEB/20	[Progress bar]																							
1085	Install Driveways / Concrete curb	4	0	20/FEB/20	25/FEB/20	[Progress bar]																							
1090	Install Roadway Base material	6	0	17/FEB/20	24/FEB/20	[Progress bar]																							
1095	First Lift of Asphalt & Watrous intersection.	1	0	27/FEB/20	27/FEB/20	[Progress bar]																							
1098	Complete Ladscape and Restoration	12	0	20/FEB/20	06/MAR/20	[Progress bar]																							
1115	3'x5' Box Culvert 213+80 to 218 Jetton Av	14	0	09/DEC/19	23/JAN/20	[Progress bar]																							
1117	Instal Buffle Box # 229 and Storm system	4	0	07/NOV/19	12/NOV/19	[Progress bar]																							
1125	Install Sidewalk/ Driveways / Curb	6	0	21/FEB/20	28/FEB/20	[Progress bar]																							
1130	Road Base material / Restoration	8	0	10/FEB/20	19/FEB/20	[Progress bar]																							
1140	Asphlat Work Manahattan to JettonAv.	1	0	13/DEC/19	13/DEC/19	[Summary bar]																							
1145	Asphalt Workist lift up to Hubert St.	1	0	13/APR/20	13/APR/20	[Summary bar]																							
1150	2,680' HDD Water Watros - Henderson	12	0	03/SEP/19	26/SEP/19	[Progress bar]																							
1155	8x5 Box Culvert 302+30 to 316+30 crossing Lois	45	0	10/FEB/20	16/APR/20	[Progress bar]																							
1157	Complete Water Main Connections at Intersections	44	24	28/FEB/20	21/MAY/20	[Progress bar]																							
1158	Asphat Work firs lift up to Lois intersection	1	0	24/APR/20	24/APR/20	[Summary bar]																							
1159	Sanitary Sewer 302 to 320 North, & South Sides	32	0	06/APR/20	18/MAY/20	[Progress bar]																							
1161	Box Culvert 320+30 to 324 Henderson	90	90	08/JUN/20	09/OCT/20	[Progress bar]																							
1162	Baffle Box and storm inles at Watrous	12	12	13/JUL/20	28/JUL/20	[Progress bar]																							
1163	Sanitary Sewer 309 to 323 North side	32	0	20/MAY/20	27/MAY/20	[Progress bar]																							
1165	Sanitary Sewer 321 to 335 South side & Clark Av.	48	0	14/APR/20	29/MAY/20	[Progress bar]																							
1166	Estrella S. Parking area Manhattan to Lois	35	35	22/JUN/20	07/AUG/20	[Progress bar]																							
1168	Storm Sewer 323 to Henderson intersect	48	0	15/JUN/20	19/AUG/20	[Progress bar]																							
1170	Install Driveways Concrete Curb	42	38	22/JUN/20	12/AUG/20	[Progress bar]																							
1174	Install Roadway base Material	38	0	15/JUN/20	05/AUG/20	[Progress bar]																							
1178	Landscape & Restoration	40	0	29/MAY/20	09/JUL/20 A	[Progress bar]																							
1180	First Lift Asphalt to Henderson Intersection	5	5	23/OCT/20	29/OCT/20	[Progress bar]																							
1188	Closed Henderson Intersection.	2	0	06/JUL/20 A	07/JUL/20 A	[Summary bar]																							
1190	Box Culvert cross Henderson 334 to 341	42	42	27/JUL/20 A	22/SEP/20	[Progress bar]																							
1195	Water, Sanitary Sewer Storm Sewer at Henderson	40	40	17/AUG/20	09/OCT/20	[Progress bar]																							
1198	Complete Storm Sewer and final connections	20	20	16/SEP/20 *	13/OCT/20	[Progress bar]																							
1200	Complete Sidewalk / Driveways / curb	40	40	25/AUG/20	19/OCT/20	[Progress bar]																							
1210	Install Roadway Base Material	48	48	12/AUG/20	16/OCT/20	[Progress bar]																							
1218	Complete Landscape /Restoration	40	40	21/SEP/20 *	13/NOV/20	[Progress bar]																							

Start date 05/JUL/19
 Must finish date 20/DEC/20
 Data date 19/JUN/20
 Run date 16/JUN/20
 Page number 1A
 © Primavera Systems, Inc.

Kimmins Contracting Corp
 Upper Penninsula Drainage Improvemt.

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Activity ID	Description	Orig Dur	Rem Dur	Early Start	Early Finish	2019																				
						AUG	SEP	OCT	NOV	DEC																
1225	Install First Lift of Asphalt	2	2	20/OCT/20	21/OCT/20	12	19	26	02	09	16	23	30	07	14	21	28	04	11	18	25	02	09	16	23	
1230	Friction Course Watrous St.	8	8	26/OCT/20	04/NOV/20																					
1255	Striping-Signs	3	3	23/NOV/20	25/NOV/20																					
1265	Punch Out Work	33	33	02/NOV/20	16/DEC/20																					
1275	Final Completion	2	2	18/DEC/20	21/DEC/20																					

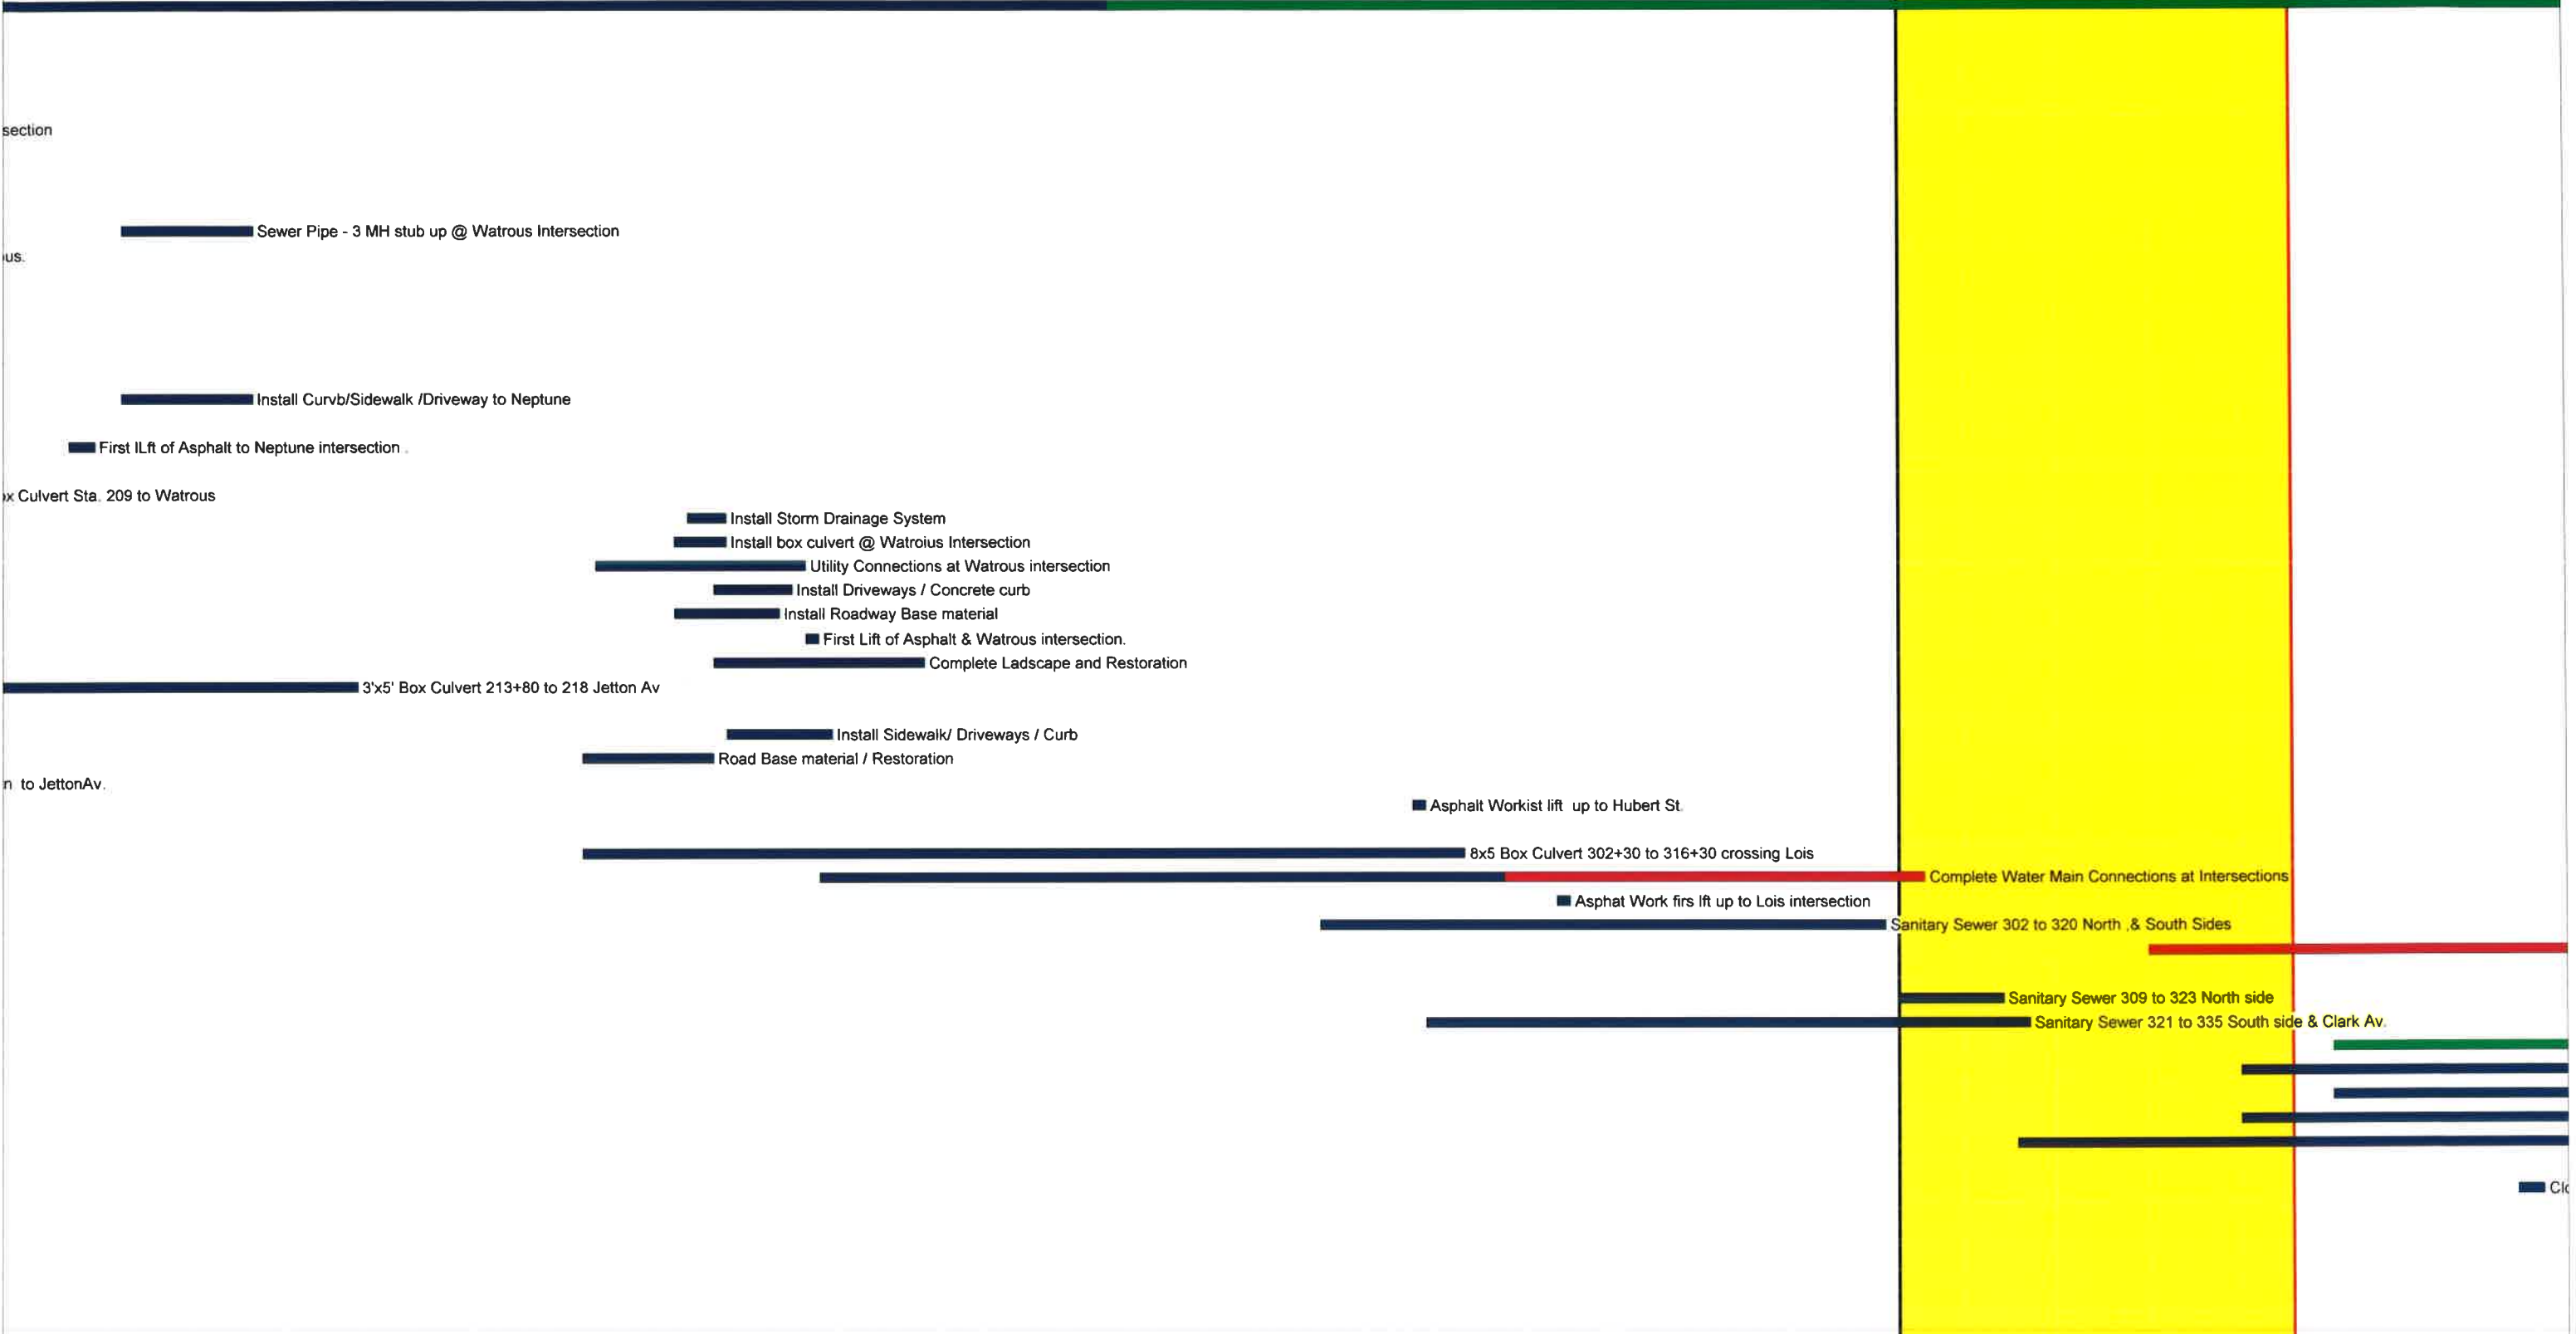


Start date 05/JUL/19
 Must finish date 20/DEC/20
 Data date 19/JUN/20
 Run date 16/JUN/20
 Page number 1B
 © Primavera Systems, Inc.

**Kimmins Contracting Corp
 Upper Penninsula Drainage Improvemt.**

- █ Early bar
- █ Progress bar
- █ Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point



PH 2- 3 MANHATTAN -WATROUS -DALE MABRY

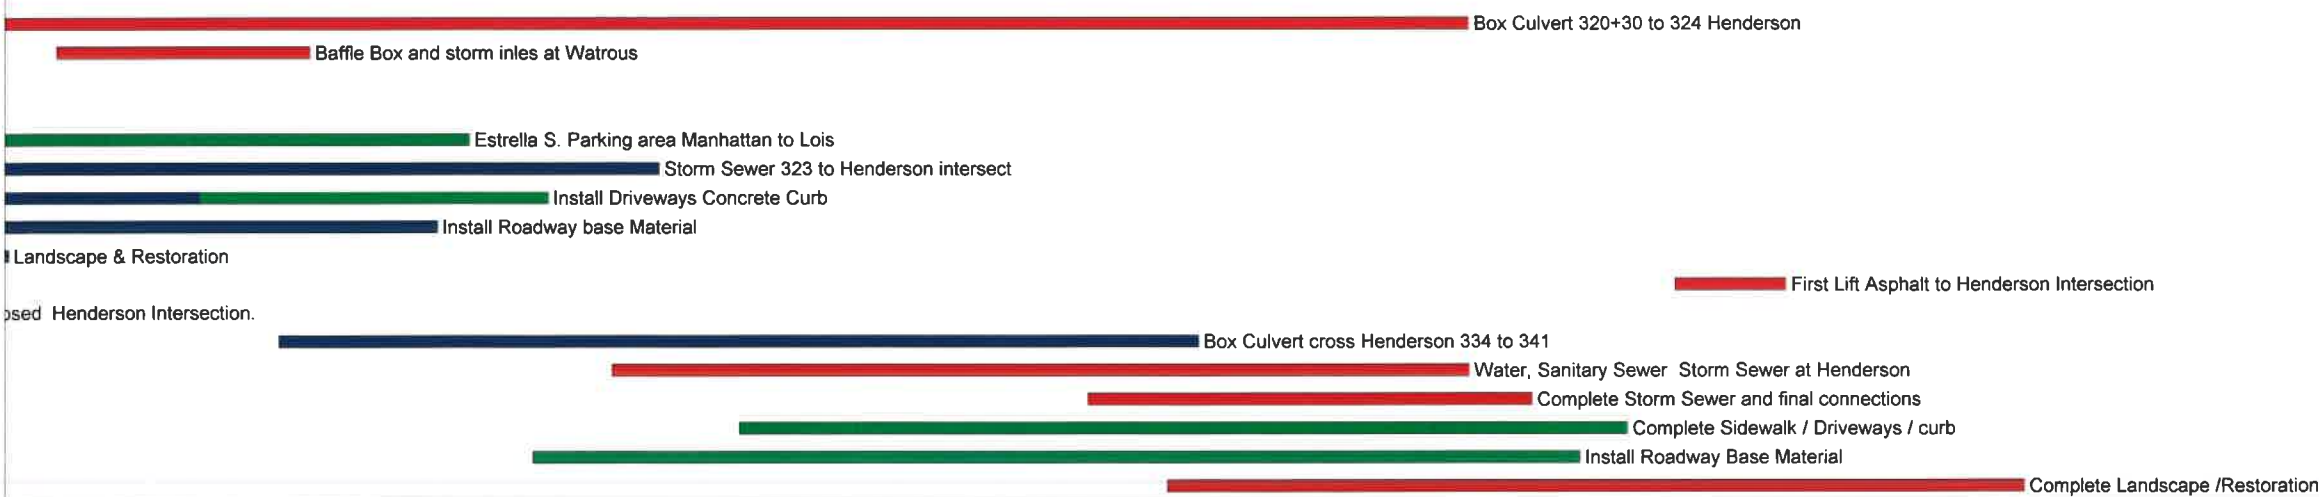

Start date	05/JUL/19
Must finish date	20/DEC/20
Data date	19/JUN/20
Run date	16/JUN/20
Page number	1C
© Primavera Systems, Inc.	

Kimmins Contracting Corp
Upper Penninsula Drainage Improvemt.

- Early bar
- Progress bar
- Critical bar
- Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point



Start date 05/JUL/19
Must finish date 20/DEC/20
Data date 19/JUN/20
Run date 16/JUN/20
Page number 2C
© Primavera Systems, Inc.

Kimmins Contracting Corp
Upper Peninsula Drainage Improvemt.

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
