


Brighton North Outfall Phase 3  
(Race to Bridge St Revision)

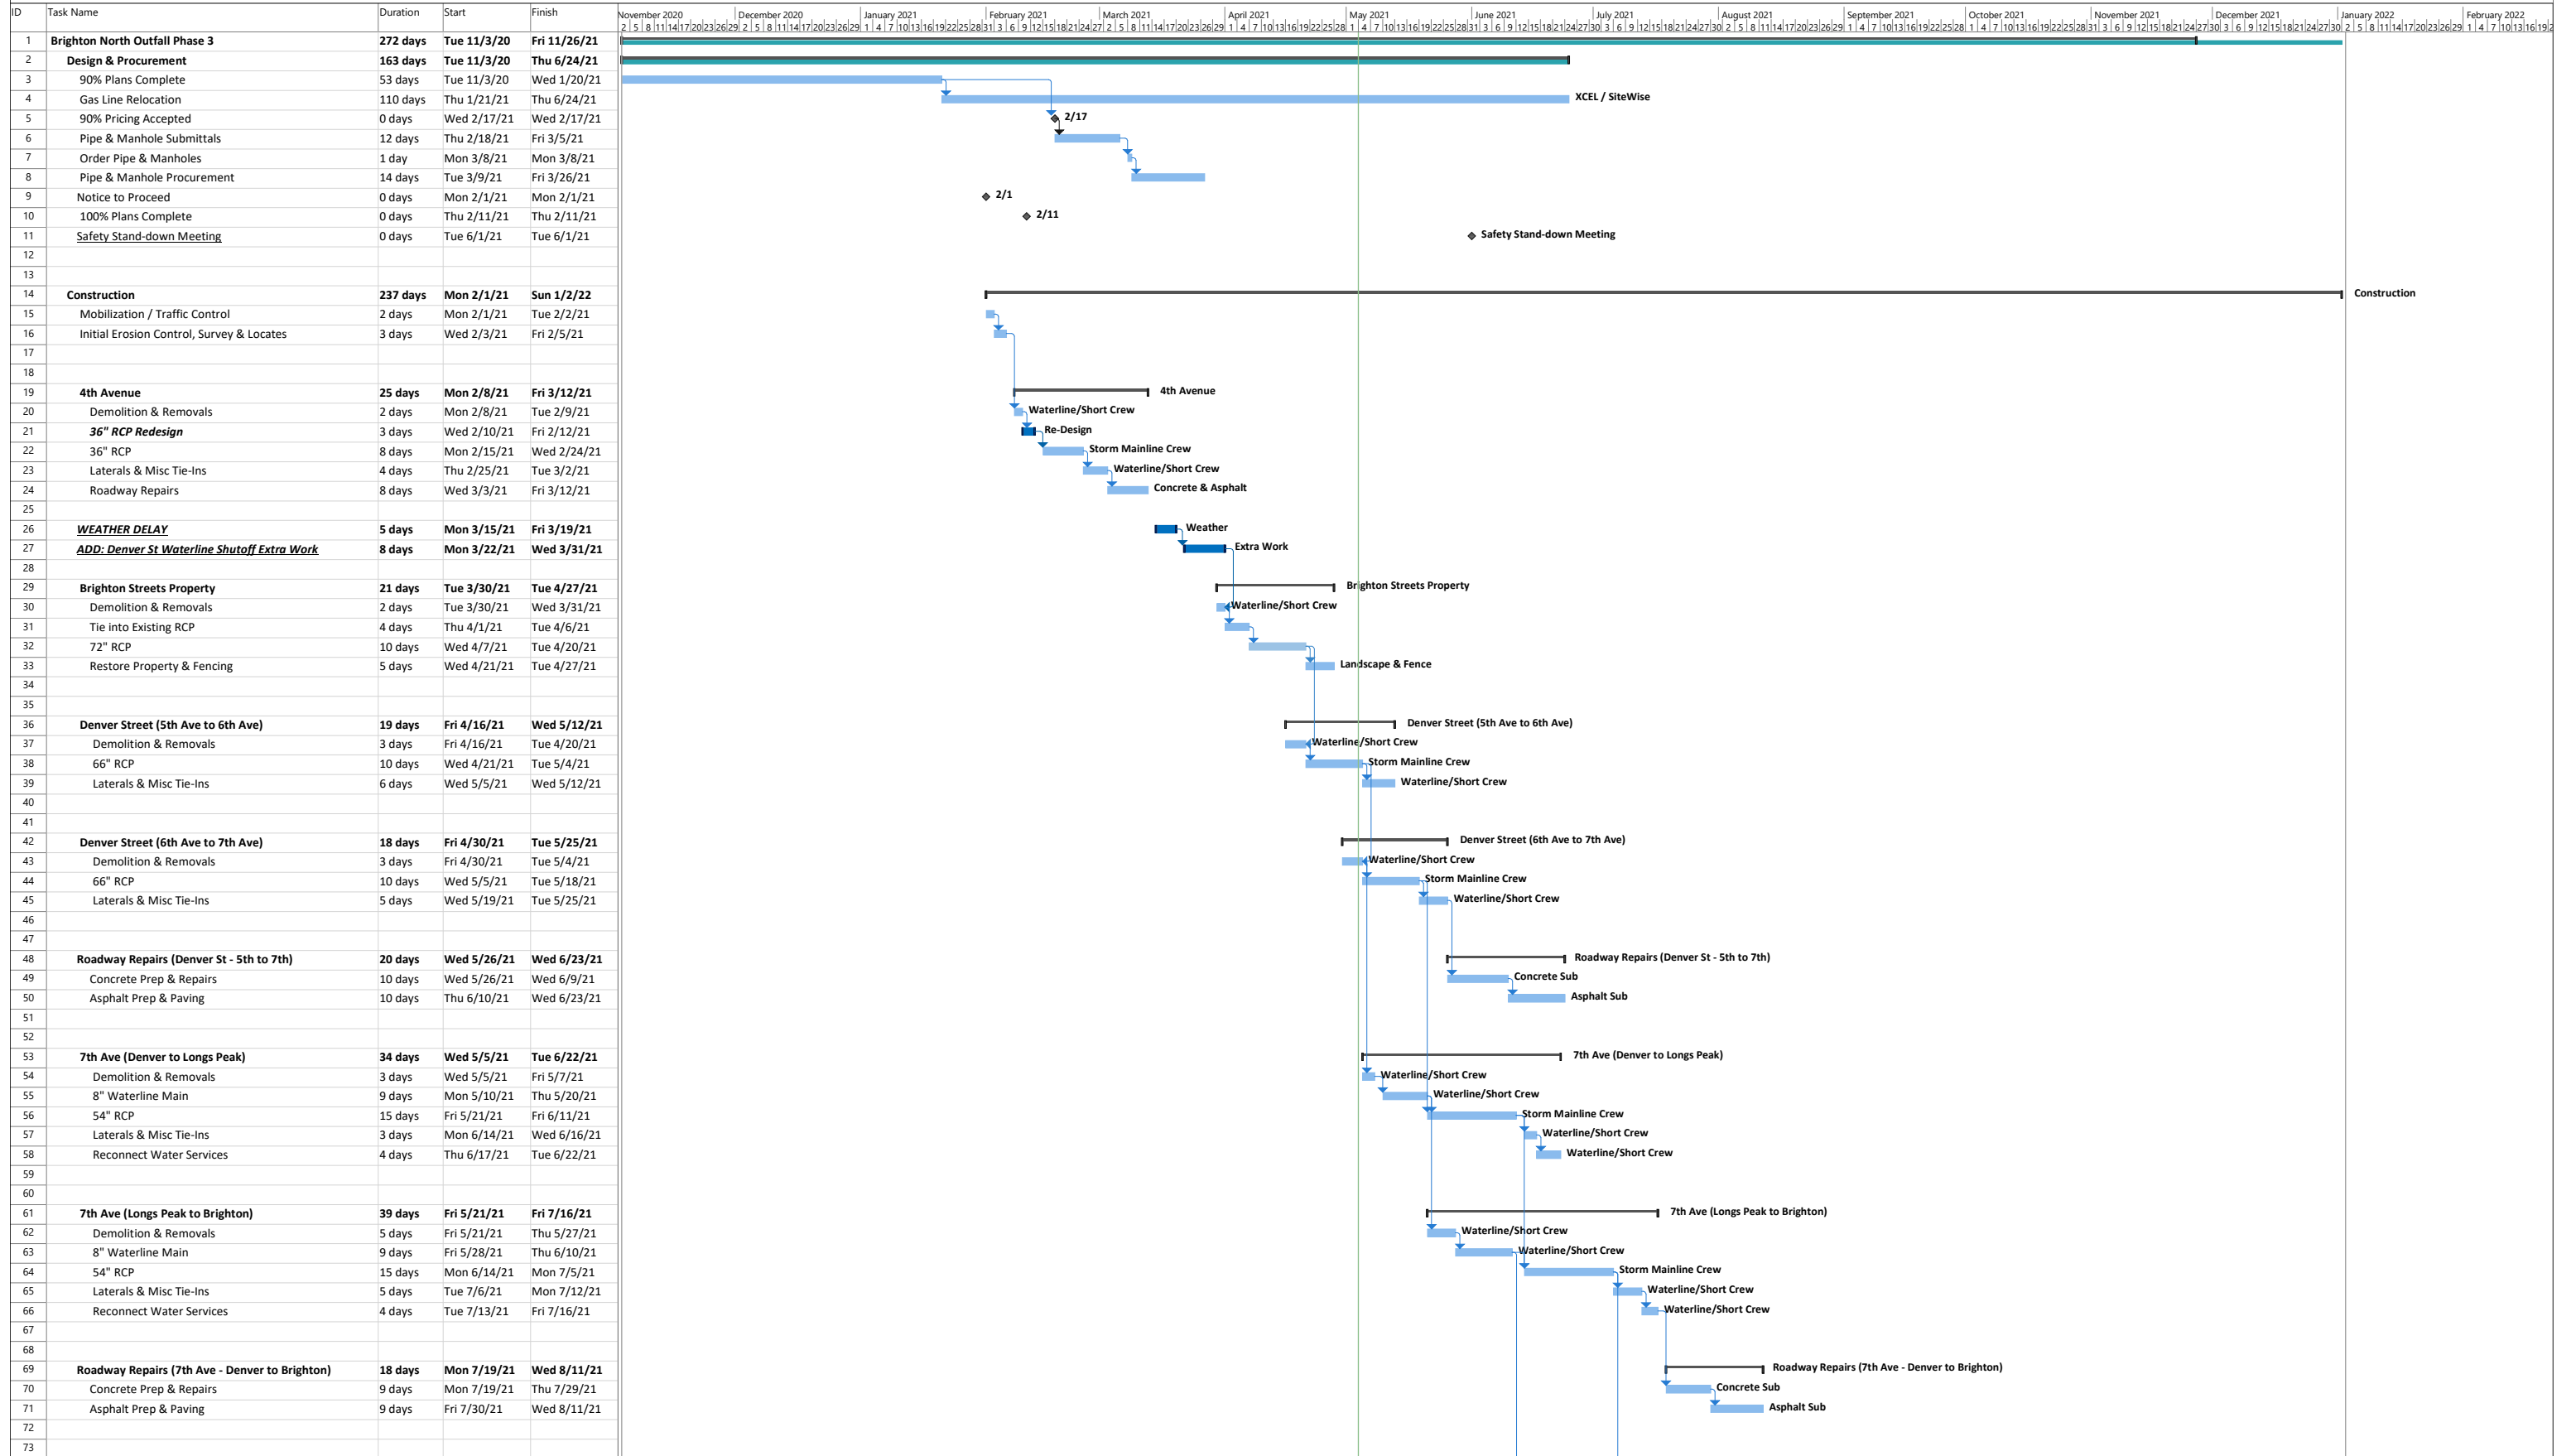

Project: Construction Schedule  
Date: Tue 5/4/21

Task Split

Milestone Summary

Project Summary Inactive Task

Inactive Milestone Inactive Summary

Manual Task Duration-only

Manual Summary Rollup Manual Summary

Start-only Finish-only


External Tasks External Milestone

Deadline Progress

Manual Progress

Brighton North Outfall Phase 3  
(Race to Bridge St Revision)

ID	Task Name	Duration	Start	Finish	November 2020	December 2020	January 2021	February 2021	March 2021	April 2021	May 2021	June 2021	July 2021	August 2021	September 2021	October 2021	November 2021	December 2021	January 2022	February 2022	
74	<b>7th Ave (Brighton to Walnut)</b>	<b>38 days</b>	<b>Fri 6/11/21</b>	<b>Wed 8/4/21</b>																	
75	Demolition & Removals	5 days	Fri 6/11/21	Thu 6/17/21																	
76	8" Waterline Main	9 days	Fri 6/18/21	Wed 6/30/21																	
77	48" RCP	15 days	Tue 7/6/21	Mon 7/26/21																	
78	Laterals & Misc Tie-Ins	3 days	Tue 7/27/21	Thu 7/29/21																	
79	Reconnect Water Services	4 days	Fri 7/30/21	Wed 8/4/21																	
80																					
81																					
82	<b>7th Ave (Walnut to Bridge)</b>	<b>38 days</b>	<b>Thu 7/1/21</b>	<b>Tue 8/24/21</b>																	
83	Demolition & Removals	8 days	Thu 7/1/21	Tue 7/13/21																	
84	8" Waterline Main	8 days	Wed 7/14/21	Fri 7/23/21																	
85	48" RCP	15 days	Tue 7/27/21	Mon 8/16/21																	
86	Laterals & Misc Tie-Ins	3 days	Tue 8/17/21	Thu 8/19/21																	
87	Reconnect Water Services	3 days	Fri 8/20/21	Tue 8/24/21																	
88																					
89																					
90	<b>Roadway Repairs (7th Ave - Brighton to Bridge)</b>	<b>16 days</b>	<b>Wed 8/25/21</b>	<b>Thu 9/16/21</b>																	
91	Concrete Prep & Repairs	6 days	Wed 8/25/21	Wed 9/1/21																	
92	Asphalt Prep & Paving	10 days	Thu 9/2/21	Thu 9/16/21																	
93																					
94																					
95	<b>Bridge Street</b>	<b>56 days</b>	<b>Wed 8/11/21</b>	<b>Thu 10/28/21</b>																	
96	Demolition & Removals	4 days	Wed 8/11/21	Mon 8/16/21																	
97	30" RCP	7 days	Tue 8/17/21	Wed 8/25/21																	
98	38"x60" RCP	7 days	Thu 8/26/21	Fri 9/3/21																	
99	7th Ave Laterals & Misc Tie-Ins	10 days	Tue 9/7/21	Mon 9/20/21																	
100	6th Ave Laterals & Misc Tie-Ins	8 days	Tue 9/21/21	Thu 9/30/21																	
101	5th Ave Laterals & Misc Tie-Ins	8 days	Fri 10/1/21	Tue 10/12/21																	
102																					
103																					
104	<b>Roadway Repairs (Bridge St)</b>	<b>7 days</b>	<b>Thu 8/26/21</b>	<b>Fri 9/3/21</b>																	
105	Concrete Prep & Repairs	5 days	Thu 8/26/21	Wed 9/1/21																	
106	Asphalt Prep & Paving	2 days	Thu 9/2/21	Fri 9/3/21																	
107																					
108																					
109	<b>Roadway Repairs (S 7th Ave / 6th Ave / 5th Ave)</b>	<b>12 days</b>	<b>Wed 10/13/21</b>	<b>Thu 10/28/21</b>																	
110	Concrete Prep & Repairs	8 days	Wed 10/13/21	Fri 10/22/21																	
111	Asphalt Prep & Paving	4 days	Mon 10/25/21	Thu 10/28/21																	
112																					
113																					
114	<b>Longs Peak Street (6th Ave to 8th Ave)</b>	<b>42 days</b>	<b>Tue 9/7/21</b>	<b>Wed 11/3/21</b>																	
115	Demolition & Removals	8 days	Tue 9/7/21	Thu 9/16/21																	
116	8" Waterline Main	10 days	Fri 9/17/21	Thu 9/30/21																	
117	30" RCP	7 days	Fri 10/1/21	Mon 10/11/21																	
118	22"x34" RCP	6 days	Tue 10/12/21	Tue 10/19/21																	
119	18" RCP	3 days	Wed 10/20/21	Fri 10/22/21																	
120	Laterals & Misc Tie-Ins	5 days	Mon 10/25/21	Fri 10/29/21																	
121	Reconnect Water Services	3 days	Mon 11/1/21	Wed 11/3/21																	
122																					
123																					
124	<b>Walnut Street</b>	<b>21 days</b>	<b>Tue 10/12/21</b>	<b>Tue 11/9/21</b>																	
125	Demolition, Removals	6 days	Tue 10/12/21	Tue 10/19/21																	
126	8" Waterline Main	7 days	Wed 10/20/21	Thu 10/28/21																	
127	30" RCP	4 days	Fri 10/29/21	Wed 11/3/21																	
128	Laterals & Misc Tie-Ins	2 days	Thu 11/4/21	Fri 11/5/21																	
129	Reconnect Water Services	2 days	Mon 11/8/21	Tue 11/9/21																	
130																					
131																					
132	<b>Denver Street (7th Ave to 8th Ave)</b>	<b>13 days</b>	<b>Fri 10/29/21</b>	<b>Tue 11/16/21</b>																	
133	Demolition & Removals	3 days	Fri 10/29/21	Tue 11/2/21																	
134	30" RCP	6 days	Thu 11/4/21	Thu 11/11/21																	
135	Laterals & Misc Tie-Ins	3 days	Fri 11/12/21	Tue 11/16/21																	
136																					
137																					
138	<b>Roadway Repairs (Longs Peak / Walnut / Denver)</b>	<b>26 days</b>	<b>Wed 11/17/21</b>	<b>Wed 12/22/21</b>																	
139	Concrete Prep & Repairs	18 days	Wed 11/17/21	Fri 12/10/21																	
140	Asphalt Prep & Paving	8 days	Mon 12/13/21	Wed 12/22/21																	
141																					
142																					
143	<b>Punch List, Project Cleanup, Demobilization</b>	<b>5 days</b>	<b>Thu 12/23/21</b>	<b>Wed 12/29/21</b>																	
144																					
145	Contract Date of Completion	0 days	Sun 1/2/22	Sun 1/2/22																	

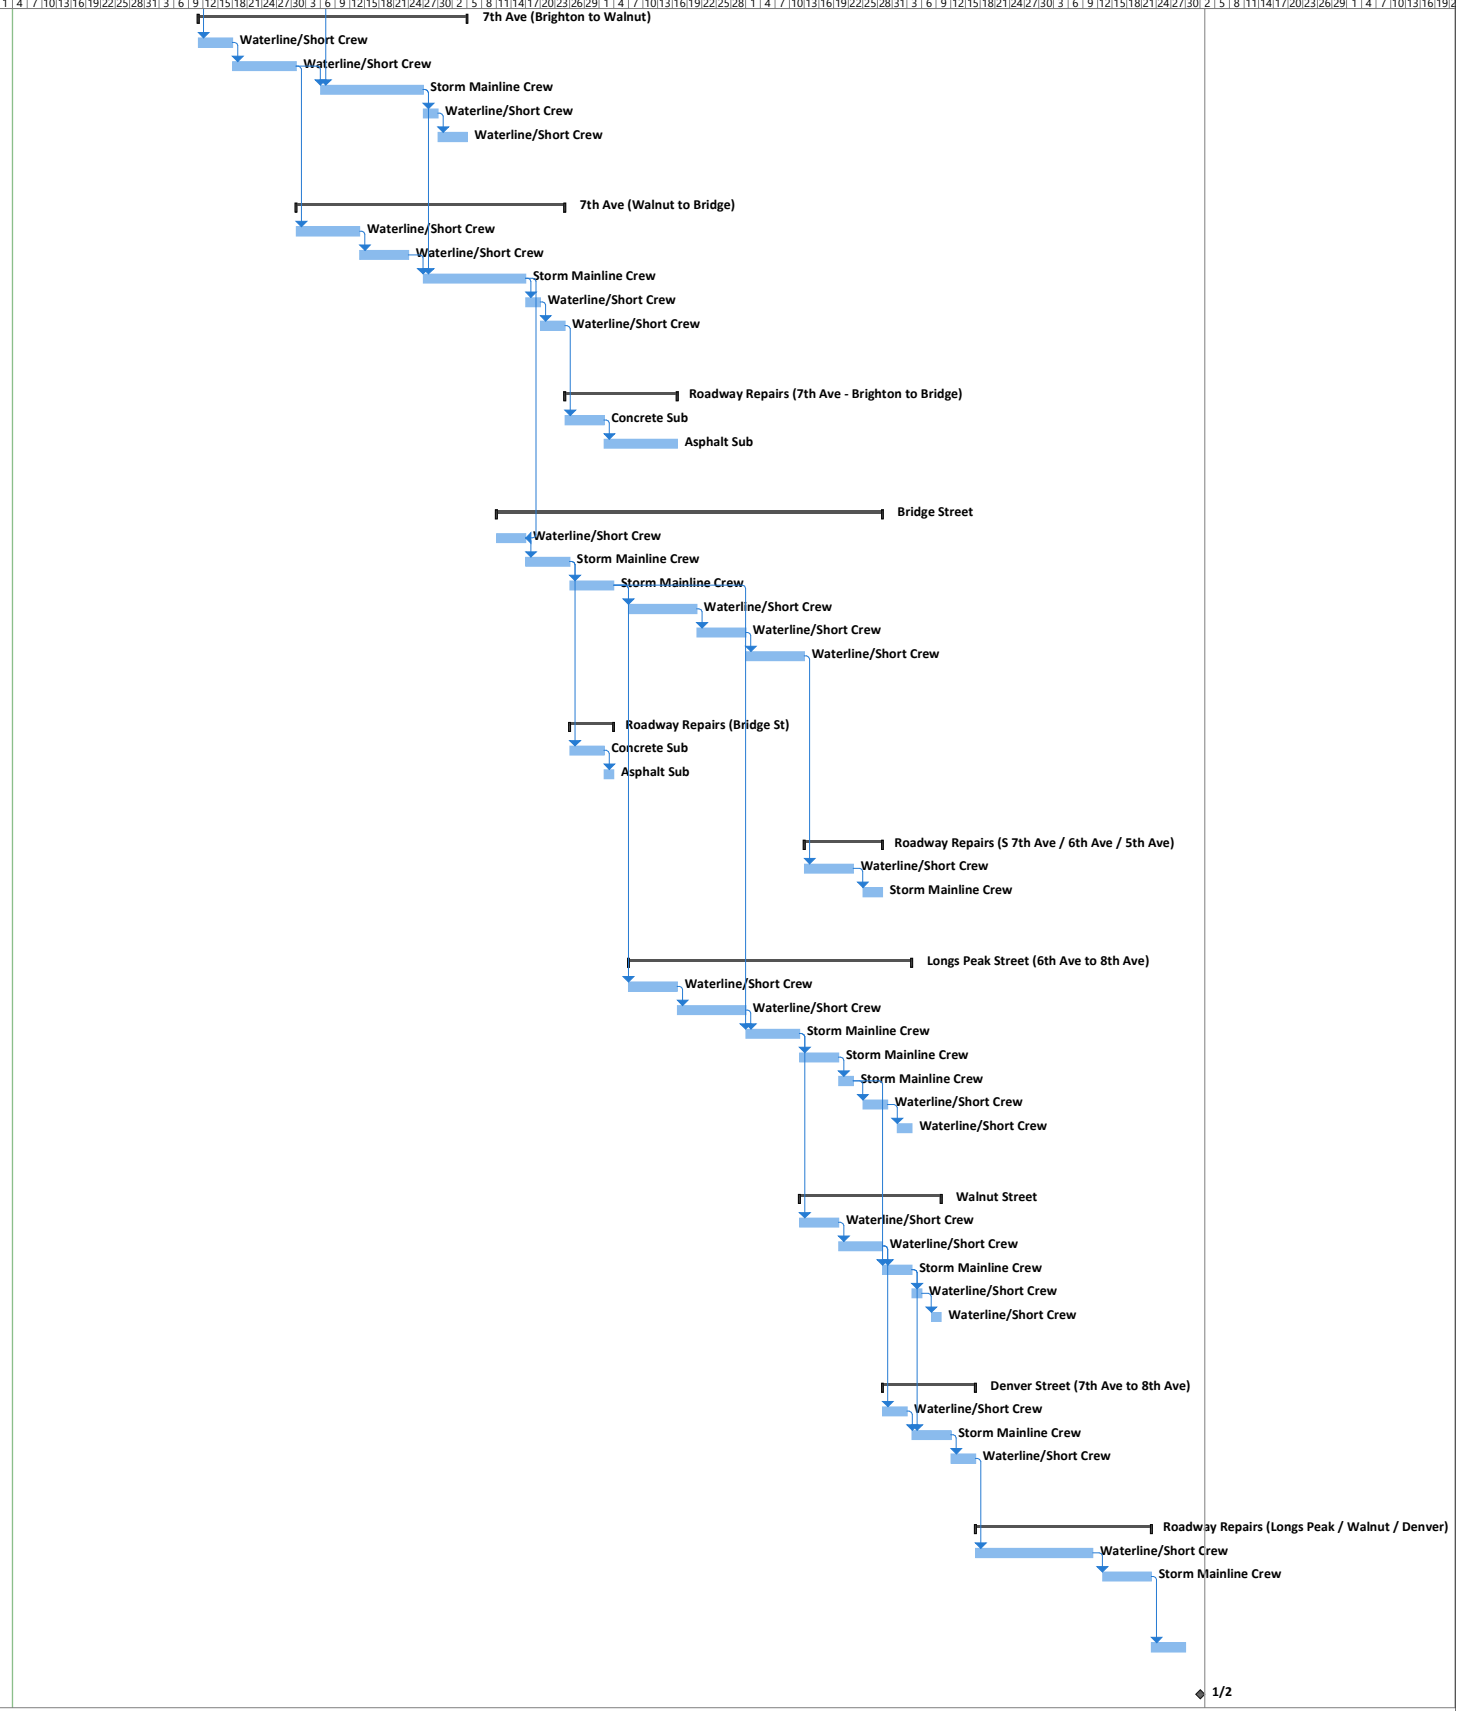

Project: Construction Schedule  
Date: Tue 5/4/21

Task Split

Milestone Summary

Project Summary Inactive Task

Manual Task Duration-only

Manual Summary Rollup Manual Summary

Start-only Finish-only

External Tasks External Milestone

Deadline Progress

Manual Progress
